REFERENCE TOOLKIT · 19 OCT 2026

1426 S Main St — Adib's Persian Rug Co

Walnut Creek, CA 94596 · APN 183-030-005 · 3D Matterport tour

22,137 sf	3,727 sf	96′-6″ × 41′-2″	16 + 3
LOT (0.51 AC)	BUILDING, 1957	FOOTPRINT, OVERALL	PARKING SPOTS ON SITE + OFF SITE

2024 ATA front design — summary

Ali Adib, P.E., ATA Engineering. All sheets on the Drawings tab.



Existing · 25 Jul 2023 · Open full size



Illustrative mockup of the 2024 ATA design (sheets A-2.1 / A-3.1): enclosed glass display bays + taller entry doors. Not to scale; not a rendering by ATA.

2024 ATA design, illustrative mockup (not to scale; not an ATA rendering) · Open full size

Square footage added

NEW ENCLOSED SPACE	WIDTH	DEPTH	AREA	BASIS
West display area	17′-0″ ±	5′-2″	≈ 88 sf	A-2.1 width · A-1.1 depth

NEW ENCLOSED SPACE	WIDTH	DEPTH	AREA	BASIS
East display area	20′-9¼″	5′-2″	≈ 107 sf	A-2.1 width · A-1.1 depth
Entry vestibule (porch enclosed)	12′-9″	≈ 13′ (scaled)	≈ 166 sf	A-2.1 width · depth scaled from A-2.1
Total newly enclosed			**≈ 361 sf**	**All non-conditioned; existing building ≈ 3,727 sf**


Summary of changes

CHANGE	EXISTING	2024 ATA DESIGN	SHEET
Walkway bays	Open, roofed walkways	Enclosed display areas, non-conditioned	A-2.1
Bay walls	None	2×6 pony wall, 3-coat ⅞″ stucco both faces, fixed tempered double-pane glazing	A-3.1
Bay floor	Walkway paving	New 4″ slab, #3 @ 12″ o.c. each way, on new footing	S-1, SD-1
Walkway posts	7×7 / 6×6 posts	New 6×6 posts (3 locations); existing headers kept	A-2.1, S-1
Entry	Open porch; (2) 3′-0″ × 6′-8″ doors	New outer glass door pair 7′-0″ × 8′-0″ (2 × 3′-6″), double-pane tempered; fixed sidelights 2′-3″± × 7′-6″; existing doors stay as inner doors → secure vestibule	A-2.1, ATA email 8/6/2024
Security doors	None	New security door from each display area to the porch	A-2.1
Porch posts	—	New P.T. 4×6 posts at the new entry	A-2.1
Roof, electrical, HVAC, site	Unchanged (all work under existing roofs; electrical as-is; non-conditioned; no site work). A-2.1 notes "new lights by others".		ATA letter 8/8/2024 · A-0.1

Plan status: permit set dated 2024-08-10, not submitted. Stamp shows CE49976 exp. 6-30-25; sheets cite 2022 codes (2025 codes in effect since 1 Jan 2026).

Roof & solar — permit S26106 (SolCore)

- **Scope:** new roof (GAF asphalt shingles) + rooftop solar, by SolCore, Inc. Separate from the ATA front work; already financed.
- **Solar:** 26.84 kW PV system on ≈ 1,286 sf of roof.
- **Storage:** 3 batteries, 34.5 kW.
- **Shingles:** GAF color deck sent 20 Jul 2026 (Charcoal, Aged Chestnut, Coastal Slate, Hickory, Sagewood, Sandalwood, Stone Gray); selection not on record.
- **Status:** issued 13 Oct 2026; no inspections yet; start date not scheduled.
- **Drawings:** SolCore's approved plans not yet obtained (city portal login or request from SolCore).

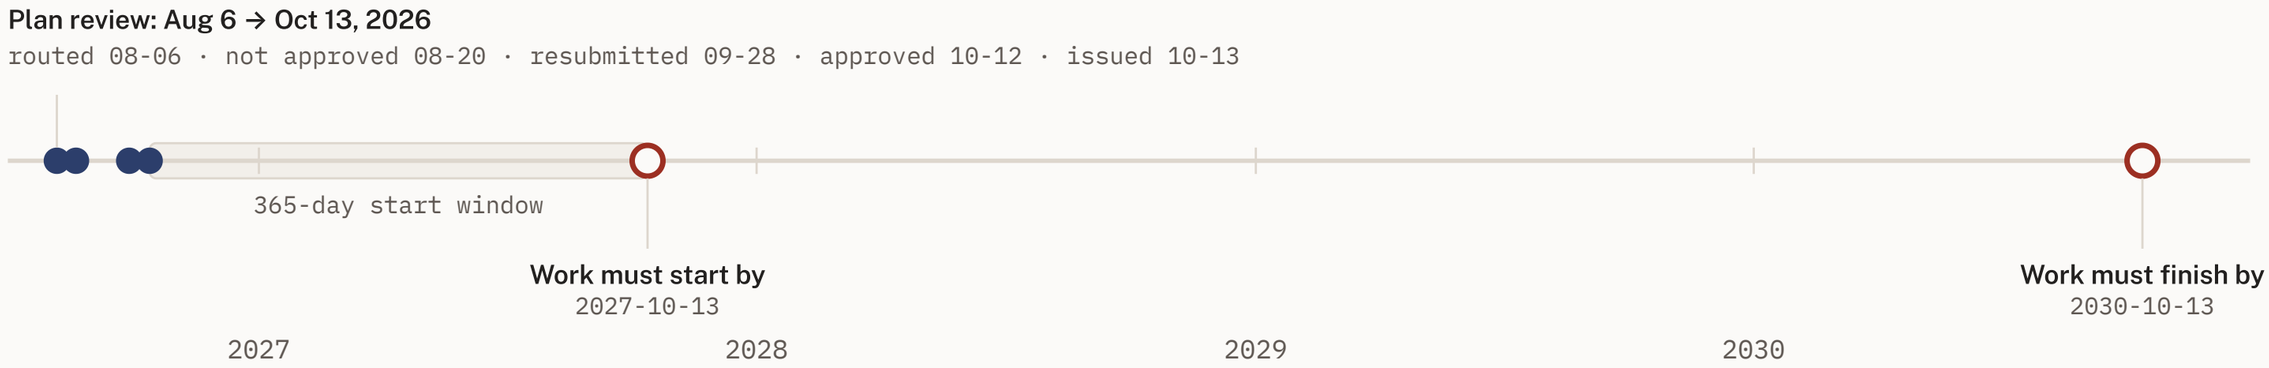

Completed Deadline

Source: City of Walnut Creek permit portal and issuance notice, 13 Oct 2026.

Site & building

ITEM	VALUE	SOURCE
Zoning / General Plan	C-R / GR	PRT 19-011, Aug 2019
Lot area	22,137 sf (city) · 20,240 sf (ATA sheet) · 20,169 sf excl. dedication (survey)	Staff report 5/2020 · A-0.1 · survey 1318
Occupancy / construction	M / IIIB, 8″ CMU + wood frame, 1 story	A-0.1
Height limit	35 ft	City letter 11/22/2019
Shared access	Recorded revocable license with neighbor (Sinovest)	License v09, 2020

ELEMENT	DIMENSION	SHEET
Overall length × depth	96′-6″ × 41′-2″	A-1.1
Entry porch width	12′-9″	A-1.1
Front walkway bays (W / E)	≈17′-0″ / ≈20′-9″ wide	A-2.1
Existing entry doors	(2) 3′-0″ × 6′-8″	ATA email 8/6/2024
Walkway posts	6×6 / 7×7, under existing headers	A-1.1, A-2.1
Roof pitches	5:12 main · 2:12 / 1:12 walkways · flat at mech.	A-1.1

Rules on this lot

CONSTRAINT	VALUE	EFFECT	SOURCE
Creek structural setback (CCCFCD)	30 ft from 2.5:1 line off creek toe	≈⅓ of existing building inside it	Staff report 5/28/2020
Creek Preserve Area	50 ft from creek centerline	Rear of lot	Staff report 5/28/2020
Street setback (GP Fig. 11)	20–30 ft, 25 ft avg	Exception "could be considered" (2020)	AppStat1 11/2019 · staff report
Future street line	50 ft from Main St centerline	Dedication on new development	AppStat2 4/2020
Parking reduction	max 20%	Staff: unlikely to support reduction (2019); 22 parking spots if retail only (2020)	PRT 2019 · staff report 2020
Parking spot location	≥10 ft from back of sidewalk	Front parking spots limited	PRT 2019 · AppStat1
Building code	2025 California codes (eff. 1 Jan 2026)	2024 ATA set cites 2022 codes	A-0.1

People

NAME	ROLE	CONTACT
Ali Adib, P.E.	Civil engineer, local lead · ATA Engineering, Redwood City	ata@ataeng.net · (650) 363-2338
Medi Adibnatanzi	Coordinator	thenatanzi@gmail.com
Ray Adib	Owner / applicant on 2024 drawings	ray@adibs.com · (925) 937-3338
David Barnes	SolCore, Inc. (CSLB 1123152)	davidbarnes@solcorepower.com · 833-765-2673
City of Walnut Creek, Building	Permits, inspections	buildingtech@walnut-creek.org · (925) 943-5834
City Planning (2019–20)	C. Griffin, A. Carreon	Griffin@ / Carreon@walnut-creek.org
